

JDA A18-B17 Pipeline Project Progress

(November 2007 – December 2007)

- Milestone achievements;
 - Completion of all four (4) riser clamps (+5 m, -9 m, -15 m and -32 m) installation at CKR platform.
 - Completion of riser installation at CKR platform
 - Completion of Emergency Shutdown Valve (ESDV) installation at CKR platform
 - Completion of 4D bend installation at CKR platform


- Current activity
 - Preparation for expansion spool and ESDV actuator installation. Expansion spool was completed the final fabrication and testing/inspection in Batam and it has now been transported to offshore and wet stored on the seabed (About 1 km from CH's platform) while ESDV actuator is now on CH's platform.

Photographs



Loading expansion spool onto cargo barge at Batam jetty

จัดวางชิ้นส่วนรองรับการขยายตัวของระบบท่อส่งก๊าซฯ บนเรือบรรทุกที่ทำเทียบเรือ บาตัม

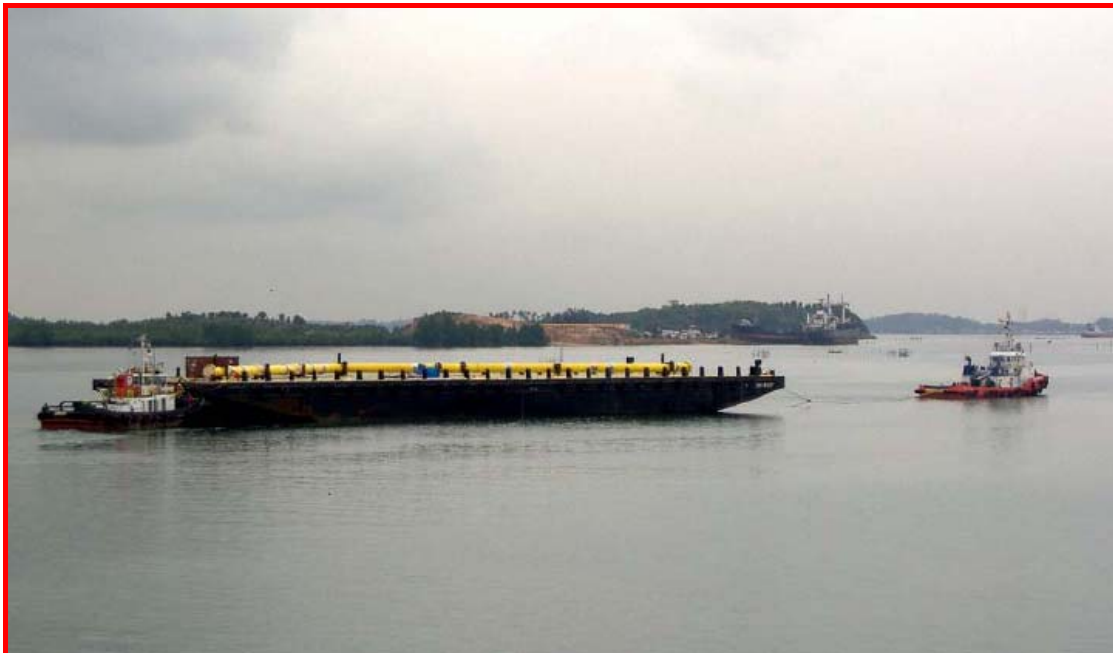

Cargo barge with expansion spool departing Batam and on the way to offshore site

เรือบรรทุกชิ้นส่วนรองรับการขยายตัวของระบบท่อส่งก๊าซฯ ออกเดินทางไปที่หน้างาน ในทะเล

Photographs



Cargo barge with expansion spool arriving at offshore site

เรือบรรทุกชิ้นส่วนรองรับการขยายตัวของระบบท่อส่งก๊าซฯ เดินทางถึงที่หน้างาน ในทะเล



Lowering expansion spool onto the seabed (Wet store)

ยกและวางชิ้นส่วนรองรับการขยายตัวของระบบท่อส่งก๊าซฯ บนพื้นทะเล
